

ALIGARH MUSLIM UNIVERSITY, ALIGARH

*Dr. N. Hasan*

Ach. in Bus. Edn. (U.S.A.), D. Litt.  
PROFESSOR & CHAIRMAN



Phones : { Office : 6247  
Res. : 6053

DEPTT. OF BUSINESS ADMINISTRATION

Date. **15.10.1988** .....

**CERTIFICATE**

This is to certify that Mr. Mohd. Eltayeb Abdalla Eltayeb has completed his thesis entitled "A COMPARATIVE STUDY OF THE PROCEDURE OF FORMULATION AND EVALUATION OF INDUSTRIAL PROJECTS IN INDIA AND SUDAN" under my supervision.

The thesis is based on the investigations and studies undertaken by the candidate and is fit for being submitted for the award of the degree of Ph.D in Business Administration. To the best of my knowledge and belief, it has not been submitted to any other University or Institution for the award of any degree or diploma.

  
Prof. Najmul Hasan  
Supervisor



**A COMPARATIVE STUDY OF THE  
PROCEDURE OF FORMULATION AND  
EVALUATION OF INDUSTRIAL  
PROJECTS IN INDIA AND SUDAN**

THESIS SUBMITTED FOR THE DEGREE OF

**Doctor of Philosophy**

IN

**Business Administration**

BY

**Mohamed Eltayeb Abdalla Eltayeb**

Under the Supervision of

*Dr. Najmul Hasan*

M. Com., Ph. D., D. Litt., Ach. in Bus. Edn. (U.S.A.)


PROFESSOR & CHAIRMAN

DEPARTMENT OF BUSINESS ADMINISTRATION


AND  
DEAN

FACULTY OF COMMERCE  
ALIGARH MUSLIM UNIVERSITY  
ALIGARH (INDIA)


1988

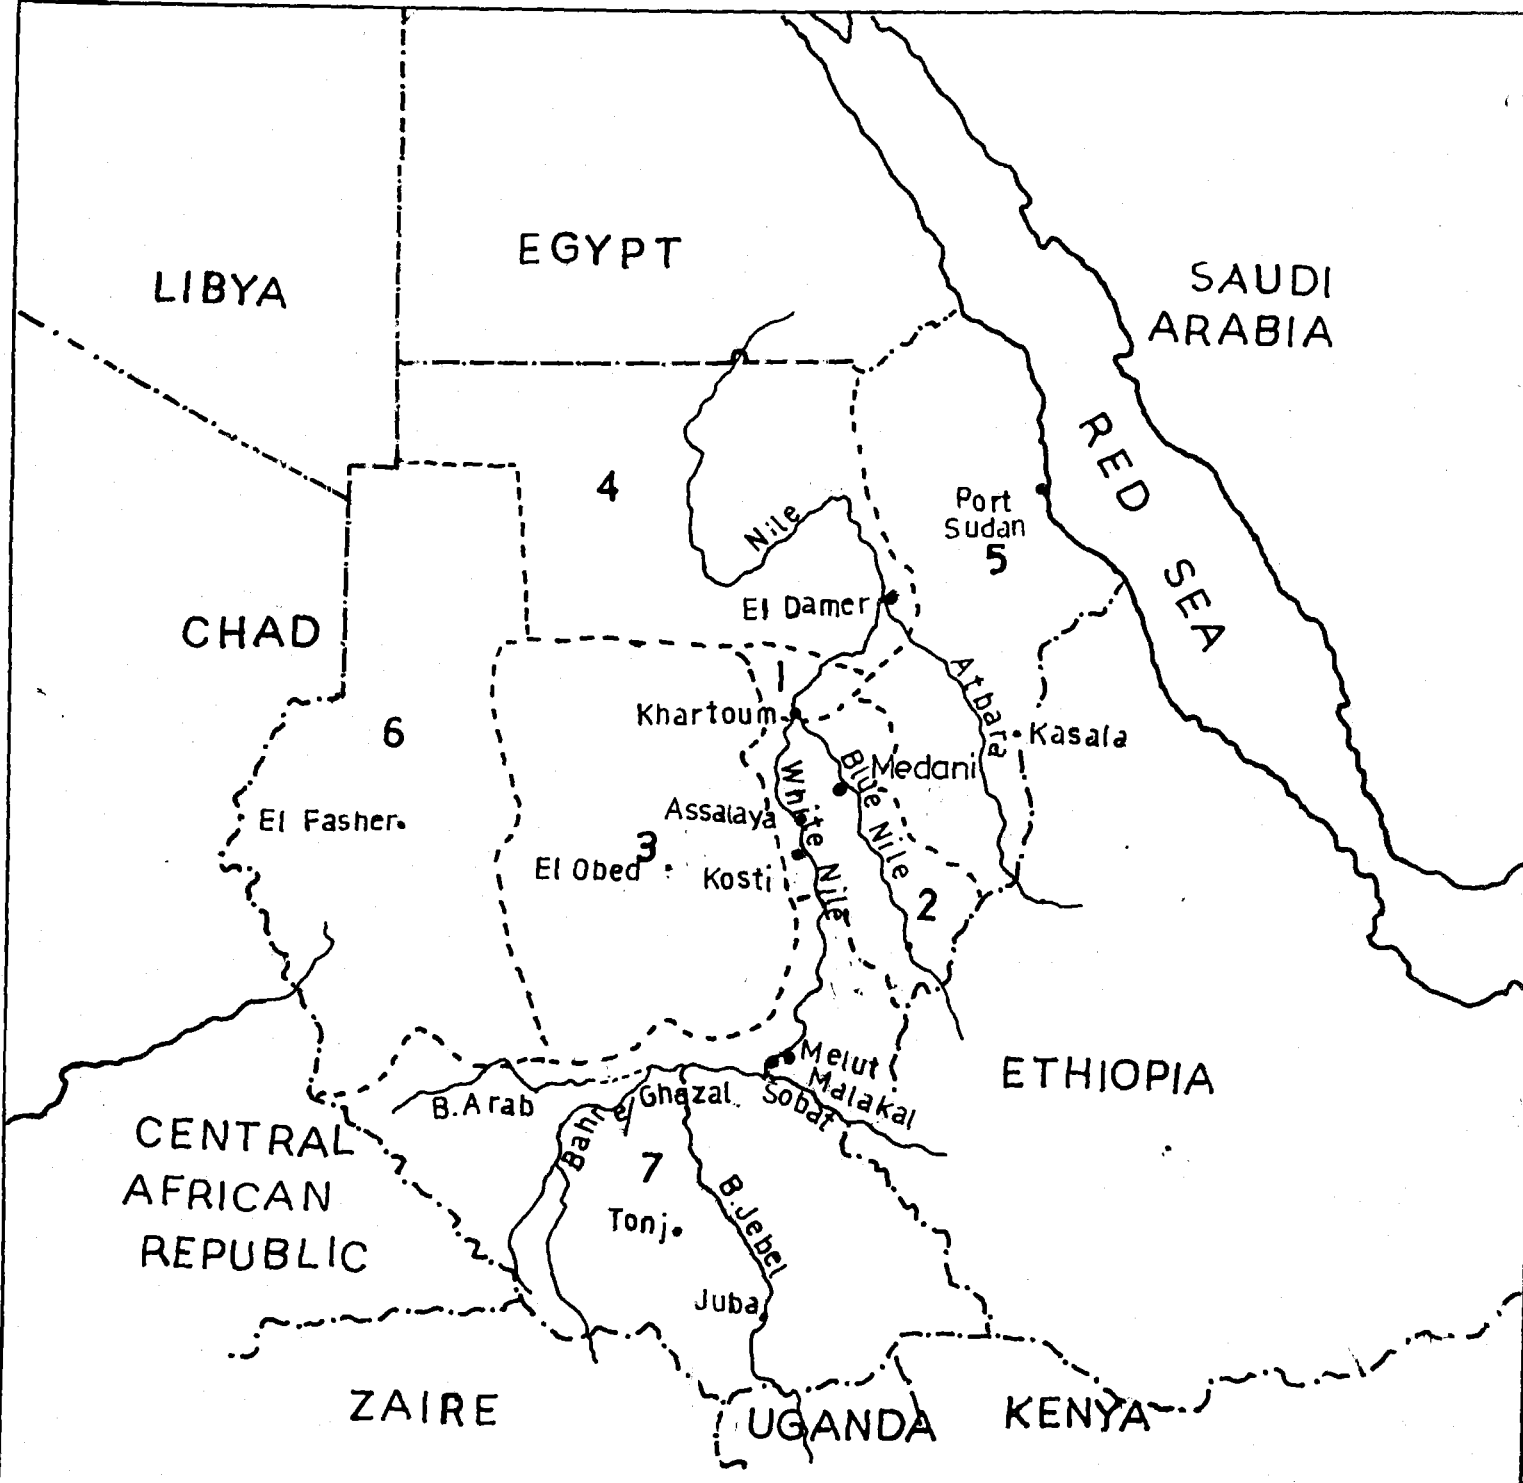

- Key**
- 1 Khartoum Commissionary
  - 2 Central Region
  - 3 Kordofan Region
  - 4 Northern Region
  - 5 Eastern Region
  - 6 Darfur Region
  - 7 Southern Region



**SUDAN**

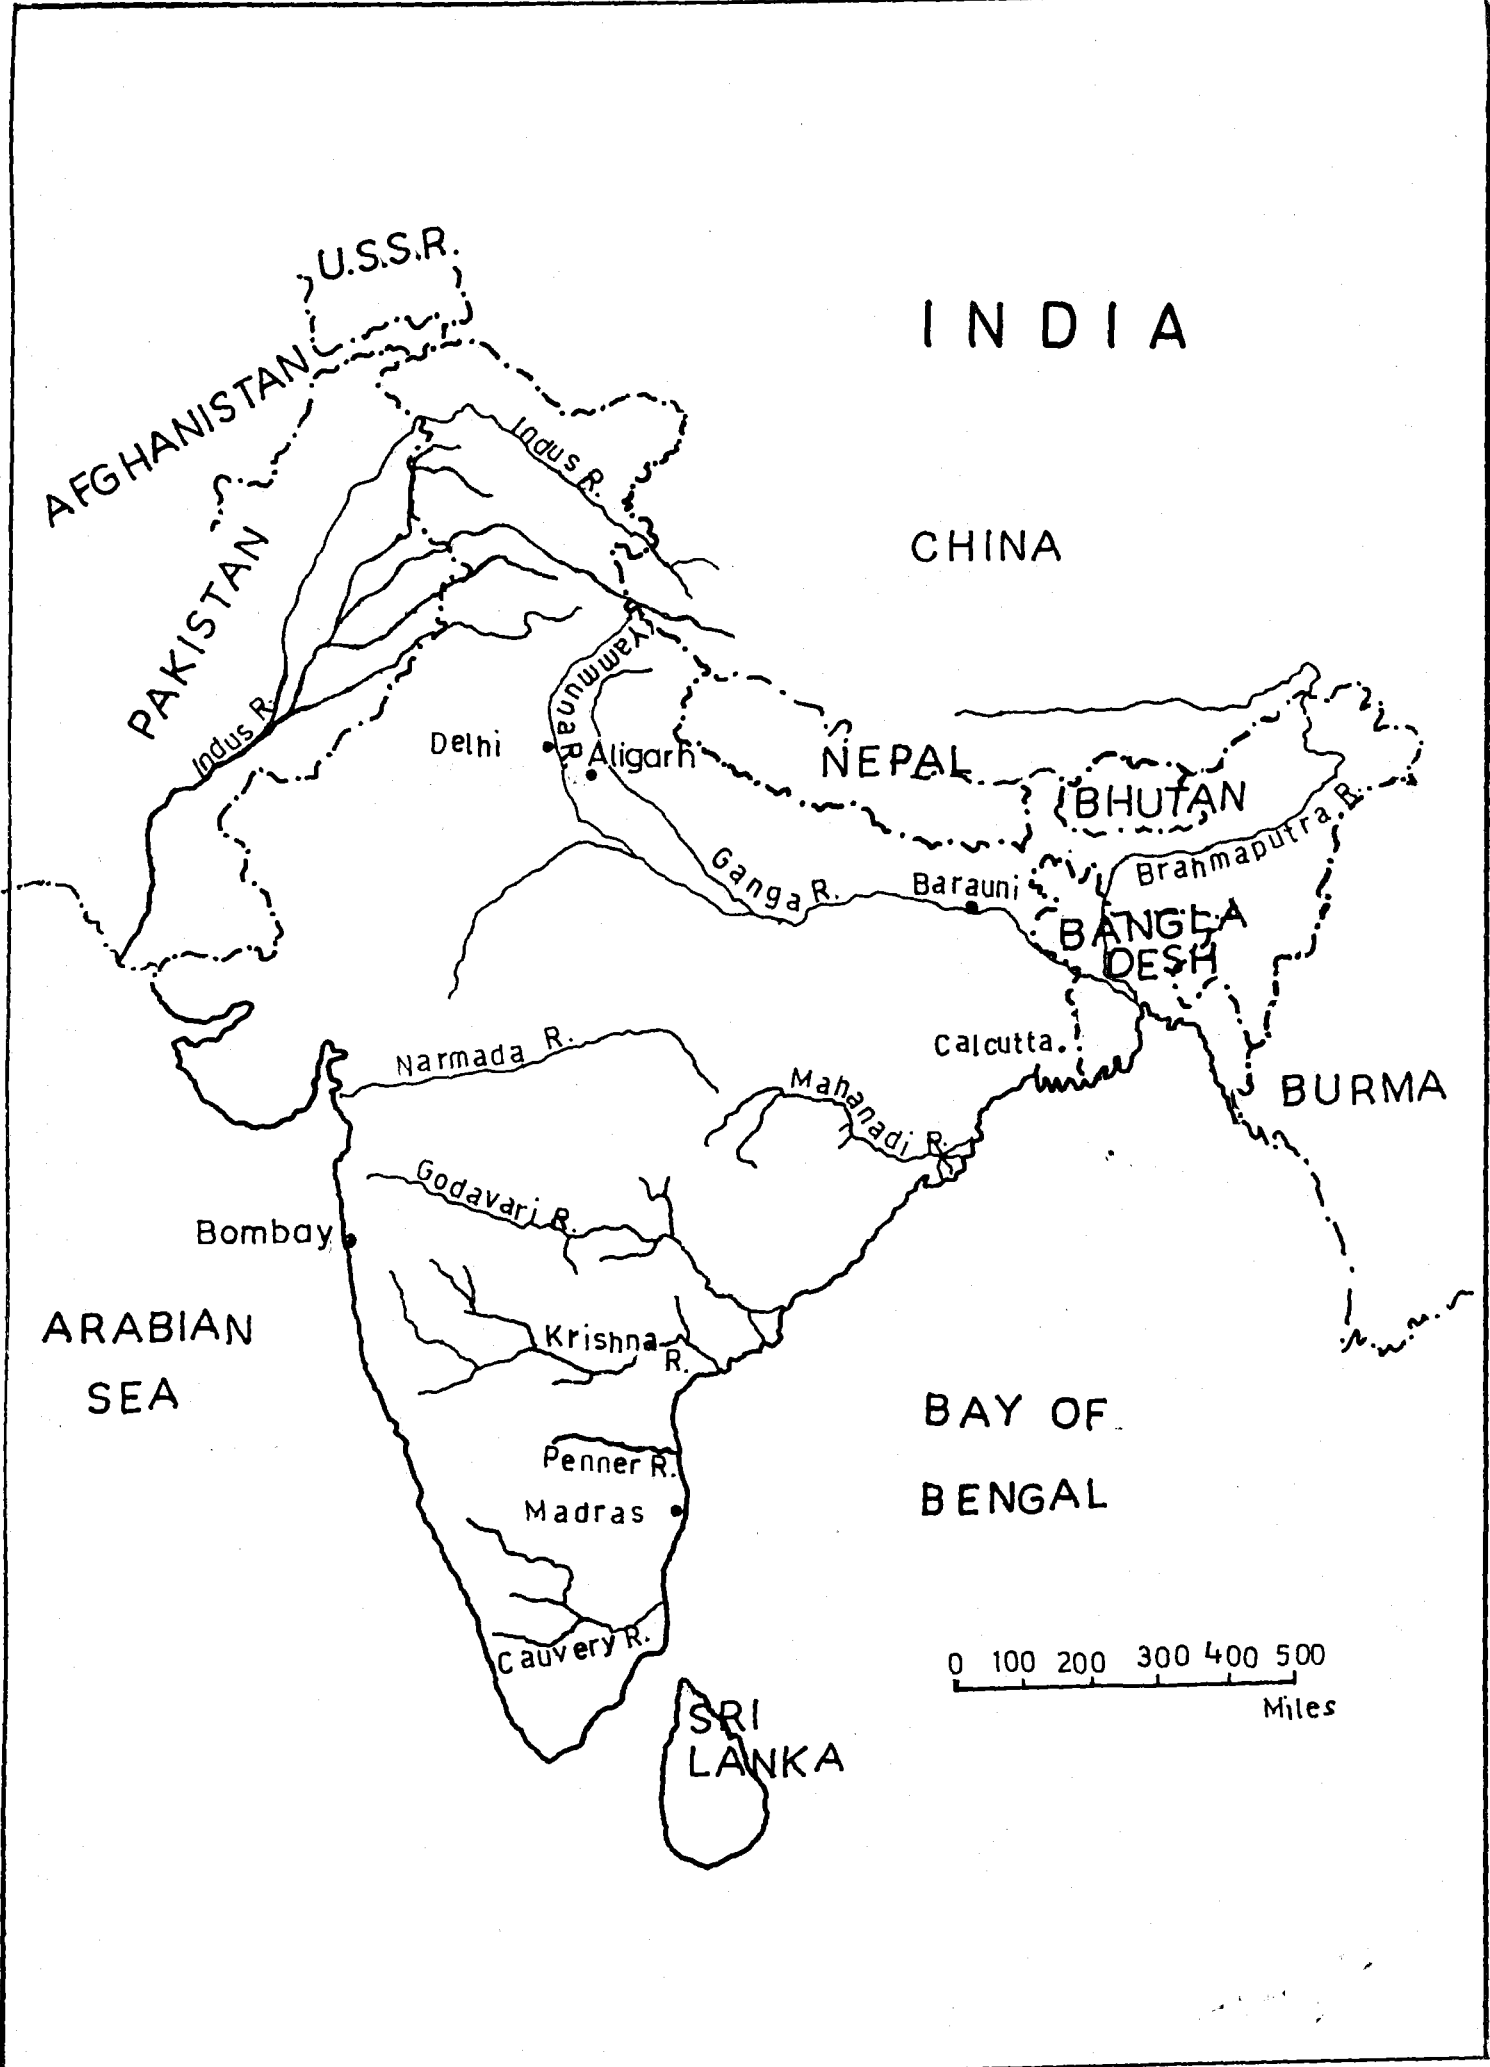

INDIA

CHINA

AFGHANISTAN

U.S.S.R.

PAKISTAN

Indus R.

Indus R.

Delhi

Aligarh

NEPAL

BHUTAN

Ganga R.

Barauni

Brahmaputra R.

BANGLA DESH

Calcutta.

BURMA

Narmada R.

Mahanadi R.

Bombay

Godavari R.

ARABIAN SEA

Krishna R.

BAY OF BENGAL

Penner R.

Madras

Cauvery R.

SRI LANKA

0 100 200 300 400 500 Miles

## ACKNOWLEDGEMENTS

I have many debts to acknowledge. Foremost, I acknowledge with respect the continuous encouragement of my parents throughout my life to acquire more knowledge.

I also take this opportunity to thank the University Grants Commission of India for awarding my scholarship which made this research work possible. Equal thanks go to the National Council for Research, Sudan, for granting me the study leave to pursue my Ph.D. programme in India.

I particularly wish to acknowledge with gratitude the guidance of my supervisor, Professor Najmul Hasan, Chairman, Department of Business Administration, and Dean, Faculty of Commerce, Aligarh Muslim University, Aligarh. His continuous encouragement, valuable suggestions and comments on approach, methodology and contents of the present study helped a lot in shaping the thesis in its present form.


The Faculty, Research Scholars and Staff Members of the Department of Business Administration, Aligarh Muslim University, Aligarh, deserve my heartiest thanks for being so friendly and helpful; thus making my stay in Aligarh a real pleasure. Equal thanks are due to my colleagues in the Economic and Social Research Council of Sudan and to my teachers in the School of Administrative Studies, University of Khartoum. Their criticisms and suggestions on methodology made in October and

November, 1985, were quite useful in preparing the present research work.

Profound thanks are also due to Professor A.Tripathy of the Indian Institute of Management, Ahmedabad, Mr. Devendra Narayan, Economic Adviser, Planning Commission of India and Mr. Adam Ibrahim El Imam, Director of the Projects Preparation Unit, Sudan. Their encouragement, discussions and valuable suggestions paved the way and helped a lot in organising my ideas.

I am also deeply indebted to many organisations which served me with data. In India, thanks go to the Ministry of Programme Implementation, the Department of Fertilisers, The Bureau of Public Enterprises, The Hindustan Fertiliser Corporation, The Industrial Development Bank of India and the Industrial Finance Corporation of India. Equal thanks are due to some organisations in Sudan, namely, the Ministry of Finance and Economic Planning, the Bank of Sudan, the Secretariat General for Investment, the Projects Bureau, the Committee of Melut Sugar Project Equipments, the Industrial Bank of Sudan and the Sudan Development Corporation.

Last, but by no means the least, I offer special appreciation to Mr. Mashhood Alam Raz who has run the hard task of typing this study.

  
MOHAMED ELTAYEB ABDALLA ELTAYEB

ALIGARH

8 October, 1988

CONTENTS

Preface	...	...	i
Acknowledgements	...	...	v
List of Tables	...	...	x
List of Figures	...	...	xi
Chapter One	A FRAMEWORK OF THE STUDY		
1.1	Preliminary Considerations		1
1.2	The Role of Project Management in Economic Development		9
1.3	Literature Review		14
1.4	Scope of the Study		24
1.5	Justification of the Study and its Relevance to Sudan		25
1.6	The Problem Stated		34
1.7	Objective of the Study		37
1.8	Research Methodology		38
1.9	Limitations of the Study		43
Chapter Two	EXAMINATION OF THE PROCESS OF PROJECT MANAGEMENT IN MANUFACTURING INDUSTRY IN SUDAN		
2.1	National Planning and Indus- trial Policies - A Historical Review ...		45
2.2	Project Formulation and Evaluation		48

2.3	Implementation System of Public Sector Manufacturing Projects	59
2.4	Licensing Apparatus and the Selection of Private Sector Manufacturing Projects	70
2.5	Term-Lending Institutions and Industrial Project Evaluation	76
2.6	Chapter Summary	82

## Chapter Three

## A CASE STUDY OF MELUT SUGAR PROJECT (SUDAN)

3.1	Project Planning	84
3.2	Feasibility Study and Contracting	86
3.3	Project Implementation	90
3.4	Time Overruns of the Project	94
3.5	Progress of the Project (1980-1987)	97
3.6	Lessons from Melut Sugar Project ...	101

## Chapter Four

## EXAMINATION OF THE PROCESS OF PROJECT MANAGEMENT IN MANUFACTURING INDUSTRY IN INDIA

4.1	National Planning and Project Identification	102
4.2	Industrial Policy and Project Licensing	104
4.3	Project Formulation	113
4.4	Project Evaluation	117
4.5	Project Implementation	125
4.6	Industrial Project Evaluation by Term-Lending Institutions	133
4.7	Chapter Summary	146

Chapter Five	A CASE STUDY OF BARAUNI FERTILISER PROJECT (INDIA)	
5.1	Project Planning	149
5.2	Detailed Engineering	152
5.3	Project Implementation	156
5.4	Time and Cost Overruns of the Project	162
5.5	Lessons from Barauni Fertiliser Project	172
Chapter Six	ANALYSIS AND COMPARISON OF THE PROCEDURES OF INDUSTRIAL PROJECT MANAGEMENT IN SUDAN AND INDIA	
6.1	Project Planning (Formulation and Evaluation)	174
6.2	Organisational Set-up	184
6.3	Project Implementation	191
6.4	Coordination - The Essence of Project Management	203
6.5	Private Sector Industrial Project Evaluation	209
6.6	Chapter Summary	219
Chapter Seven	CONCLUSIONS AND POLICY IMPLICATIONS	
7.1	Conclusions	223
7.2	Policy Implications	235
APPENDICES	...	246
BIBLIOGRAPHY	...	262

LIST OF TABLES

Table 3.1	Melut Sugar Project Schedule Revisions and Costs	....	89
Table 5.1	Completion Dates of Equipments Erection (Barauni Fertiliser Project)		155
Table 5.2	Activity Chart of the Refinery Gas Boiler Erection (Barauni Fertiliser Project)	...	163
Table 5.3	Activity Chart of the Piping Works (Barauni Fertiliser Project)		166
Table 5.4	Time and Cost Overruns of Barauni Fertiliser Project		169
Table 5.5	Break-up of Cost Overruns (Barauni Fertiliser Project)		172

---

LIST OF FIGURES

Fig. 2.1	Organisation Chart of the Projects Preparation Unit (PPU)	54
Fig. 2.2	Process-Flow Chart of Government Project Proposals (Sudan)	56
Fig. 2.3	Organisation Chart of Government Projects Implementation - Sudan (1973) ...	63
Fig. 2.4	Process-Flow Chart of the Request of Payment (Sudan)	68
Fig. 3.1	Organisation Chart of Melut Sugar Project	91

---
